



Programme financé
par l'Union européenne



PROGRAMME
**ÉCONOMIE
BLEUE** EN ALGÉRIE
Pêche et Aquaculture



Session 3

Gestion administrative et Coordination partenariale dans les projets collaboratifs EU

INNOfluence

Agenda de la formation

Session 1

Monter une proposition gagnante

- Facteurs clés de succès (1 jour)
- Elaborer une proposition gagnante (1 jour)

Session 2

Elaboration & gestion d'un budget de projet UE

- Elaboration du budget d'un projet UE (1/2 jour)
- Gestion financière (1/2 jour)

Session 3

Gestion de projets UE

- Gestion administrative (1/2 jour)
- Coordination partenariale (1/2 jour)

Session 4

Coaching projets UE

- Constitution offre, volet théorique (1 jour)
- Constitution d'offres, volet pratique (1 jour)

Sommaire Session 3 – M3.1 (a.m.)

- ✓ M3.1 : Gérer, communiquer et rapporter efficacement auprès de la CE
- ✓ Objectif : Configuration telle que mentionnée dans le cahier des charges, mettre en place des outils de gestion, gestion administrative des contrats et des relations avec l'organisme de financement, gestion des Livrables et milestones et stratégie de communication vers l'extérieur, Dissémination et exploitation des résultats
- ✓ Programme :
 - ✓  09h00 – 09h30 : Mise en place d'outils de gestion de projets collaboratifs UE
 - ✓  09h30 – 10h15 : Gérer, communiquer et rapporter efficacement auprès de la CE
 - ✓  10h30 – 11h00 : Gestion des conflits
 - ✓  11h00 – 11h45 :
 - ✓  11h45 – 12h30 : Q&A, Exercices et synthèse de la matinée

Sommaire Session 3 – M3.2 (p.m.)

- ✓ M3.2 : Gestion des Partenariats Transnationaux
- ✓ Objectif : Construire et entretenir son réseau de partenaires sur le long terme.
- ✓ Programme :
 - ✓  13h45 – 14h30 : Réseautage et intégration dans un consortium
 - ✓  14h30 – 15h30 : Témoignages
 - ✓  16h15 – 17h00 : Synthèse et fin de formation

Mise en place d'outils de gestion

Pour organiser et piloter un projet collaboratif européen

Session 3 – M3.1

Mise en place d'outils de gestion efficaces

Matrice RACI

**Clarifier les
responsabilités**

Suivi des actions

**Assurer une
traçabilité
rigoureuse**

Gantt Chart

**Piloter le planning
du projet**

Matrice RACI

- ✓ Clarification des rôles et responsabilités → Moins de conflits et d'ambiguïtés ;
- ✓ Fluidité dans la prise de décision → Identification claire de qui valide quoi ;
- ✓ Amélioration de la coordination → Meilleure communication entre les partenaires ;
- ✓ Suivi plus efficace → Meilleure visibilité sur qui doit faire quoi et à quel moment.

Dénomination	Explication
Responsable (R)	Personne responsable de l'exécution i.e. qui réalise la tâche. Il peut y en avoir plusieurs.
Accountable (A)	Personne qui valide et est redevable du bon aboutissement de la tâche.
Consulted (C)	Personne impliquée pour donner un retour d'expertise avant l'exécution.
Informed (I)	Personne qui doit être tenue au courant de l'avancement, mais sans rôle actif.

- ✓ Comment mettre en place une matrice RACI efficace ?
 - ✓ Lister toutes les tâches du projet (par exemple en lien avec le Gantt Chart) ;
 - ✓ Identifier les rôles clés pour chaque tâche ;
 - ✓ Éviter les doublons : chaque tâche doit avoir un seul "A", mais peut avoir plusieurs "R", "C" ou "I" ;
 - ✓ Faire évoluer la matrice en fonction de l'évolution du projet.

Matrice RACI : exemple

Tâche	Coordinateur	WPL	Partenaires	Gestionnaire financier	Coachs
Rédaction de la Section 1 de la proposition					
Rédaction de la Section 2 de la proposition					
Rédaction de la Section 3 de la proposition					
Validation du budget					
Soumission de la proposition					
Reporting					

Fichier de suivi des actions

Caractéristique

- Clair
- Traçable
- Suivi régulier
- Évolutif

Structure

- ID Action
- Date de création
- Objet
- Responsable
- WP concerné
- Priorité
- Date de revue
- Statut
- Commentaires

Bonnes pratiques

- Mettre à jour le fichier chaque semaine
- Attribuer une responsabilité claire
- Fixer des échéances réalistes
- Suivre les blocages
- Utiliser des outils adaptés (e.g. MS project)

Suivi des actions : exemple


#	Week	Date Création	Thème	Level	WP	Objet	Qui	Date_ objectif	Open/Close	Date de Revue	Observations
A13	27	07/07/2023	Propal	Naval Group	WPs	MAJ du WBS suite discussion avec TNO	FaD		Close		
A14	27	07/07/2023	Propal	Naval Group	WPs	Initialisation des objectifs de Milestones à atteindre dans E=MCM	EID		Open		Check de conformité avec les attentes de l'UE à faire par Mamadou puis partage avec les WPLs
A21	27	07/07/2023	Partenariat	NGB	N/A	Trouver substitut à Cafa (Estonie) + renforcer la Pologne	MaB	13/07/2023	Open		

Un suivi rigoureux des actions **garantit** que toutes les parties prenantes **sont alignées** et que le projet avance de manière fluide et maîtrisée;

Gantt Chart

Objectifs

- Vision globale du projet
- Meilleure gestion du temps
- Clarification des rôles
- Optimisation des ressources
- Meilleure coordination

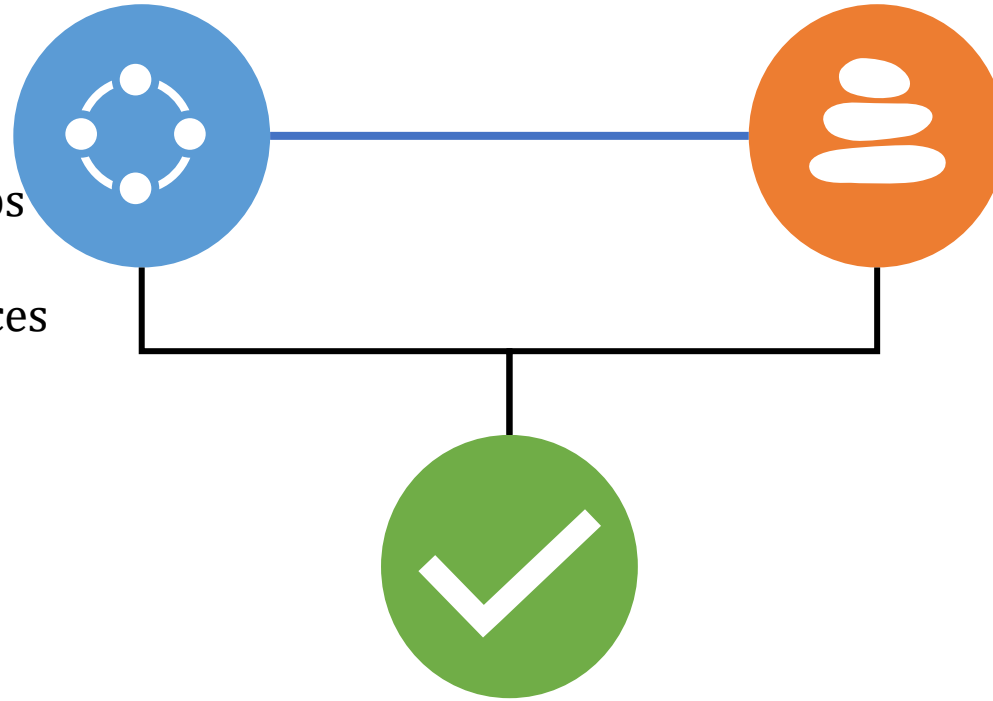

Éléments clés

- Tâches
- Durée
- Dépendances
- Responsables
- Avancement
- Jalons (Milestones)

Bonnes pratiques

- Définir des tâches claires et atteignables (éviter les tâches trop générales).
- Mettre à jour régulièrement le Gantt pour refléter l'état d'avancement réel.
- Anticiper les risques et les retards pour ajuster la planification en conséquence.
- Partager le Gantt avec toute l'équipe et s'assurer qu'il est bien compris.

Gantt Chart : exemple

Progressing work			Planning		Year 1								Year 2				Year 3				Year 4				Year 5																
Workpackages & Tasks			Leader	M start	M end	1	3	4	6			9	10	12	18	24		29	30	36		42	47	48		51	52	54		59	60										
1	Project Management Activities		ULILLE	M01	M60	D1.1	D1.12	D1.2 & D1.13 & D1.14			D1.3 & D1.15			D1.4 & D1.16	D1.5 & D1.17		D1.6		D1.7 & D1.18		D1.8 & D1.19		D1.9 & D1.20		D1.10 & D1.21			D1.11 & D1.22													
2	OnshoreClean Energy Production, Storage and Distribution		H2V	M01	M60											MS1 & MS2 & MS3		MS4																							
2.1	Green Hydrogen Production		H2V	M01	M60											D2.1 & D2.7				D2.5		D2.11		D2.13		D2.15															
2.2	Decarbonization and greening solutions for rail transport in the waterborne multimodal hub		FRET	M01	M36											D2.2				D2.8																					
2.3	Greening solutions for maritime transport		GPMD	M01	M36											D2.3				D2.9																					
2.4	Greening solutions for inland transport		GPMD	M18	M48												D2.6				D2.4																				
2.5	Greening solutions for road transport		CNJ	M01	M36											D2.4				D2.10																					
3	Smart Logistics Management		AAU	M01	M48	MS5										MS6 & MS7 & MS8																									
3.1	Implementation of energy optimisation for freight flows		PRO	M01	M48											D3.1				D3.5				D3.12																	
3.2	Inter-operable energy optimization for multimodal hub operations		AAU	M01	M48											D3.4				D3.8				D3.11																	
3.3	Energy-Based Road Fleet Management		UNIMED	M01	M48											D3.2				D3.6				D3.9																	
3.4	Modal Shift Management		ULILLE	M01	M48											D3.3				D3.7				D3.10																	
4	Smart Mobility		GAUSSIN	M01	M60	MS9										MS10	MS11		MS12																						
4.1	Development & Implementation of tractors with engine powered by H2		GAUSSIN	M01	M60											D4.4				D4.10				D4.15		D4.21															
4.2	Development & Implementation of reach stackers with engine powered by H2		H&Y	M01	M60											D4.5				D4.11				D4.16		D4.22															
4.3	Energy planning for vehicle		ULILLE	M01	M48											D4.3				D4.9				D4.20																	
4.4	Intelligent control for energy management		IMPERIAL	M01	M42											D4.1		D4.6												D4.13											
4.5	Efficient implementation of intelligent control systems		IMPERIAL	M24	M48																		D4.17																		
4.6	Predictive Maintenance for smart mobility		IMPERIAL	M01	M48											D4.2				D4.8				D4.18																	
4.7	Evolution of mobility criteria for large public communication		POLE	M24	M42																	D4.14																			
4.8	Smart rail mobility		FRET	M01	M48																	D4.7				D4.19															
5	Environmental impact assessment		SKUT	M01	M48	MS10																																			
5.1	Sensor network for emission determination		UGent	M01	M42											D5.1				D5.4				D5.7																	
5.2	High-resolution emission modelling		UGent	M18	M48															D5.5 & D5.6				D5.9																	
5.3	Local pollution impacts in a European and global context		SKUT	M12	M48												D5.3				D5.10																				
5.4	Environmental impacts of new technologies in port hubs		SKUT	M06	M48									D5.2						D5.8		D5.12																			
6	Socio-economic, supporting activities for sustainability		UU	M01	M60											MS15																									
6.1	Formation of a Business Advisory and Innovation Transition Stakeholder Group		AMS	M12	M48															D6.3				D6.8		D6.12															
6.2	A longitudinal Case Study on the Lighthouse Pilot		UU	M01	M48													D6.2				D6.5				D6.9															
6.3	Policy and Financial Support Scoping Study		UTU	M03	M36											D6.1				D6.4																					
6.4	MIMO2SA Lighthouse& fellow Business Models		UU	M24	M60																	D6.6				D6.11		D6.13													
6.5	Entrepreneurship development from MIMO2SA's innovation		POLE	M25	M48																			D6.10																	
7	Smart Energy Management		IDE	M01	M60											MS16																									
7.1	Energy Optimisation Platform Design		IDE	M01	M30											D7.2			D7.4		D7.6																				
7.2	Digitalisation of the port's energy grid		PRO	M01	M30											D7.1			D7.5		D7.7																				
7.3	Optimisation Platform Implementation		IDE	M24	M42																D7.9		D7.11																		
7.4	Integration and Testing		IDE	M24	M48																D7.12																				
7.5	Data protection & Sharing and Management		PRO	M01	M60											D7.3				D7.8				D7.10		D7.13															
8	Dissemination & Communication and Exploitation results		ITRANS	M01	M60																																				
8.1	Dissemination and Communication strategy		ITRANS	M01	M60											D8.3					D8.4				D8.5				D8.6		D8.7										
8.2	Communication tools		ITRANS	M01	M60	D8.1	D8.2																																		
8.3	Dissemination and Communication of results		ITRANS	M01	M60											D8.8																									
8.4	Dissemination and communication events		ITRANS	M01	M60																																				
8.5	Exploitation project results		CMATH	M12	M60											D8.9 & D9.10			D8.11		D8.12				D8.13		D8.14														
9	Replicability & Governance for master plan		CMATH	M12	M60										MS17										MS18																
9.1	Replicability Process		CMATH	M18	M60										D9.1				D9.2				D9.5		D9.9		D9.10														
9.2	Impact of hydrogen-driven cargo handling equipment in the European port sector		UTU	M36	M48																		D9.6																		
	Sustainable Port policy recommendations and strategic Master plan for the Green Port		AMS	M12	M48														D9.3				D9.8																		
	Replication of the result for the Energy optimisation platform		IDE	M24	M42																	D9.4																			
	Replicability outside of the MIMO2SA Consortium		UTU	M36	M48																			D9.7																	
10	Inclusive common actions & sister projects collaboration		UTU	M01	M60																																				
10.1	Identification and selection of the sister projects and other on-going projects and initiatives to link with		CMATH	M01	M24											D10.1													D10.16												
10.2	Common actions with sister projects		ULILLE	M07	M60										D10.2						D10.3				D10.4		D10.5														
10.3	International Multidisciplinary Green Deal Think Tank		UTU	M25	M60																						D10.8		D10.9												

Rapporter vers la Commission Européenne

Quelques exemples réels de projets

Session 3 – M3.1

Paielement sur la plateforme F&T

Lien de connexion
Plateforme Commission
Européenne pour les
financements des
projets collaboratifs
européens Horizon
Europe

<https://ec.europa.eu/info/funding-tenders/opportunities/portal/screen/home>

SyGMA - System for Grant Management - Windows Internet Explorer

(EXTERNAL) ?

Grant Management Project Periodic Report

Project 555555 ABC R&I test project

HORIZON 2020

Period No: 1 Duration (months): 6
Reporting Period : [01/07/2014 - 31/12/2014]

Beneficiary 1: Test account

Legal Name: Test account legal entity
PIC: 999777555 Status: VALIDATED
Legal Address: ABC street, BBB city, AAA country

Financial Statements

slide to select beneficiary

Financial Statement

Financial information from contact

No contribution requested? ☐ Yes ☒ No

Financial Statements

Period	Adjustment	Requested Contribution
01/07/2014 - 31/12/2014 (Period No '1')	No	100,000.00 €

Financial Statement for period '1' (01/07/2014 - 31/12/2014)

Eligible costs: 0

Cost Category	Total	Actions
a) Direct personnel costs declared as actual costs	30,000.00 €	☐
b) Direct personnel costs declared as unit costs (average costs)	0.00 €	☐
d) Direct costs of subcontracting	65,000.00 €	
e) Direct costs of providing financial support to third parties	0.00 €	
f) Other direct costs	3,000.00 €	☐
h) Indirect costs (= 0.25 * (a + b + f - o))	8,000.00 €	
j) Total costs (= a + b + d + e + f + h)	106,000.00 €	
k) Receipts	0.00 €	
m) Maximum EU contribution (100%)	106,000.00 €	
n) Requested EU contribution	100,000.00 €	
z) Requested EU contribution eligible for CFS	106,000.00 €	

Additional Information for indirect costs:

Use of 'costs of in-kind contributions not used on premises?' (o) ☐ Yes ☒ No

Les livrables sur la plateforme F&T

SyGMa - System for Grant Management - Google Chrome

ec.europa.eu/research/participants/grants-app/reporting/DLV-723246

n00a5m8d (EXTERNAL)

Grant Management

Project Continuous Report

HOW TO

IA

THE FRAMEWORK PROGRAMME FOR RESEARCH AND INNOVATION

Call: H2020-MG-2016-2017

Topic: MG-2.2-2016

Unit: CINEA/C/03

Summary for publication

Deliverables Ethics, DMP, Other Reports

Milestones

Critical Risks

Publications

Disseminat... and Communic...

Intellectual property rights (IPR)

Innovation

SME Impact

Gender

ABS Regulation

Deliverables, Ethics, DMP, Other Reports

For each Deliverable, a single file (max 52MB) can be uploaded

Show Filters Clear Filters

WP No	Del Ref.	Del No	Title	Description	Lead E	Nature	Dissemin	Est. Del. Da	Rev. Due Da	Receipt Dat	Approval Date	Status	
WP1	D1.1	D1	Project Procedure Manual	T01.3 - The Project Procedure Manual will outli...	CET	Report	Confide	30 Sep 20'		14 Nov 20	06 Dec 2018	Approved	
WP2	D2.1	D2	Quality Assurance Procedun	T02.1 - Composition of the TQA, definition of t...	CET	Report	Confide	30 Sep 20'		14 Nov 20	07 Dec 2018	Approved	
WP3	D3.1	D3	Installation of Advisory Groi	T03.3 - Composition of MAG, scope of collaborat...	CMT	Report	Confide	30 Nov 20		26 Jan 20'	07 Dec 2018	Approved	
WP3	D3.2	D4	First report on Technology 1	T03.1, T03.2, T03.3 - Documentation of first TT...	CMT	Report	Confide	31 May 20		04 Jul 201	07 Dec 2018	Approved	
WP3	D3.3	D5	Updated report on Technolo	T03.1, T03.2, T03.3 - updated documentation of ...	CMT	Report	Confide	31 May 20		28 Jun 20'	20 Jun 2020	Approved	
WP3	D3.4	D6	Final Report on Technology	T03.1, T03.2, T03.3 - Final documentation of TT...	CMT2	Report	Confide	31 May 20		31 May 20	01 Dec 2021	Approved	
WP4	D4.1	D7	Plan and Structure for the I	T04.1 - Report on the specification, installati...	BAL	Report	Confide	31 Jan 20'		12 Mar 20'	07 Dec 2018	Approved	
WP4	D4.2	D8	First online version of the K	T04.2 - Documentation of the online version of ...	BAL	Website	Confide	31 May 20		06 Aug 20'	10 Dec 2018	Approved	
WP4	D4.3	D9	Final online version of the I	T04.3 - Documentation of new features (if appli...	BAL	Website	Confide	30 Nov 20		30 Nov 20	10 Dec 2018	Approved	
WP4	D4.4	D10	Terms of Reference for the	T04.1 - Requirement specification for a Maritim...	CMT	Report	Confide	31 May 20		28 Jun 20'	20 Jun 2020	Approved	
WP4	D4.5	D11	Online version of the Innov	T04.2 - Documentation of the online version of ...	BAL	Website	Confide	31 May 20		29 May 20	20 Jun 2020	Approved	
WP4	D4.6	D12	Innovation Platform popula	T04.2 - Documentation and analysis of informati...	CMT2	Website	Confide	30 Sep 20'		29 Nov 20'	01 Dec 2021	Approved	
WP5	D5.1	D13	Public Project Website	T05.1 - This deliverable consists of the public...	CMT	Website	Public	30 Nov 20		19 Dec 20	10 Dec 2018	Approved	
WP5	D5.2	D14	Project Flyer	T05.1 - The printed flyer will provide basic in...	CMT	Website	Public	31 May 20		23 Jul 201	10 Dec 2018	Approved	
WP5	D5.3	D15	First Concept of sustainable	T05.2 - Terms of Reference for a sustainable RA...	CMT	Report	Confide	30 Nov 20		30 Nov 20	10 Dec 2018	Approved	

Suivi de la visibilité

SyGMA - System for Grant Management - Google Chrome

ec.europa.eu/research/participants/grants-app/reporting/DLV-723246

Grant Management

Project Continuous Report

Horizon 2020

Call: H2020-MG-2016-2017

Topic: MG-2.2-2016

Unit: CINEA/C/03

Summary for publication

Deliverables, Ethics, DMP, Other Reports

Milestones

Critical Risks

Publications

Dissemination and Communication

Intellectual property rights (IPR)

Innovation

SME Impact

Gender

ABS Regulation

HOW TO

Dissemination & Communication Activities

Specify the total funding amount used for Dissemination and Communication activities linked to the project

Total Funding Amount

100,000.00 €

Specify the number of Dissemination and Communication activities linked to the project for each of the following categories

Organisation of a Conference	8
Organisation of a Workshop	13
Press release	9
Non-scientific and non-peer-reviewed publication (popularised publication)	22
Exhibition	9
Flyer	7
Training	0
Social Media	2
Website	1
Communication Campaign (e.g. Radio, TV)	3
Participation to a Conference	30
Participation to a Workshop	28
Participation to an Event other than a Conference or a Workshop	3
Video/Film	20
Brokerage Event	1
Pitch Event	1
Trade Fair	13
Participation in activities organised jointly with other EU project(s)	4
Other	5

Specify the estimated number of persons reached, in the context of all dissemination and communication activities, in each of the following categories

Scientific Community (Higher Education, Research)	700
Industry	300000
Civil Society	0
General Public	700000
Policy Makers	500
Media	700
Investors	0
Customers	200000
Other	0

Validate

Suivi des publications

SyGMA - System for Grant Management - Google Chrome

ec.europa.eu/research/participants/grants-app/reporting/DLV-723246

n00a5m8d (EXTERNAL)

Grant Management

Project Continuous Report

HOW TO

IA

HORIZON 2020

Call: H2020-MG-2016-2017

Topic: MG-2.2-2016

Unit: CINEA/C/03

Summary for publication

Deliverables, Ethics, DMP, Other Reports

Milestones

Critical Risks

Publications

Dissemination and Communication

Intellectual property rights (IPR)

Innovation

SME Impact

Gender

ABS Regulation

Publications

SAVE

☐ This project does not currently have any scientific publication

Suggested publications from OpenAIRE (14 publications)

☐ Include previously discarded publications

No.	Type	Title	Authors	Title of the Journal/Proc./Book	Date of Acceptance	DOI	Repository Link	Actions
1	Other	Project video						
2	Other	Project Flyer						
3	Article in Journal	Numerical modelling approach for considering effects of surface	Nafar Dastgerdi, J.; Sheibanian, F.; Rei		01/12/2020			
4	Article in Journal	2nd FIBRESHIP WORKSHOP - RAMSSES demo case	Billaudeau, Emilien	instname:Scipedia SL	01/01/2019			
5	Other	Committee V.3: Materials and Fabrication Technology	Lennart Josefson, Stephen van Duin, B	Progress in Marine Science and Technology - Volume	01/01/2018			

Project publications (15 publications)

Show Filters Clear Filters

Publications + Manually add publication


No.	Type	Title	Authors	Title of the Journal/Proc./Book	Number, date or freq. of the Journal/Proc./Book	Is Peer-reviewed?	Is Open Access?	DOI	Repository Link	Actions
1	Publication	RAMSSES - Realisation and Demonstration of Advanced Ma	Matthias Krause, Frank Roland, Ca	Proceedings of 7th Transport Research Arena T	7	Yes	Green	10.5281/zenodo.1483140		
2	Chapter in i	Committee V.3: Materials and Fabrication Technology	Lennart Josefson, Stephen van Dui	Progress in Marine Science and Technology - Vi	Volume 2	Yes	Green	10.3233/978-1-61499-864-8-143		
3	Publication	Ongoing R&D Projects in Uljanik - Aktivni istraživački i ra	Dundara, Dani; Kuzmanović, Obrac	Book of proceedings of the 23rd Symposium oi	1	Yes	Green	10.5281/zenodo.2635221		
4	Publication	Demonstrating the use of advanced materials and rethink	Krause, Matthias; Paboeuf, Stépha	Proceedings of 8th Transport Research Arena T	8	Yes	Green	10.5281/zenodo.3937379		
5	Publication	A "Fast Track to Approval" Process for Innovative Maritime	stephane paboeuf; Arnold de Bruij	Practical Design of Ships and Other Floating St	1	Yes	Green	10.5281/zenodo.3941526		
6	Article in Jo	On the benefits of metallic additive manufacturing for pr	Muller, Pol; Rückert, Guillaume; Vi	Sixth International Symposium on Marine Prop	6	Yes	Green	10.5281/zenodo.2635190		
7	Article in Jo	Stress magnification factor for angular misalignment betw	Federica Mancini, Heikki Remes, J	Welding in the World	64/4	Yes	Gold	10.1007/s40194-020-00866-7		
9	Publication	MODULAR DECK SYSTEM FOR RORO VESSELS - RAMSSES H2	Vito Radolovic; Jospi Andrisic	Proceedings of 24th Symposium on the Theory	1	Yes	Green	10.5281/zenodo.4134530		
10	Article in Jo	Numerical modelling approach for considering effects of	J. Nafar Dastgerdi; J. Nafar Dastge	Journal of Constructional Steel Research	175	Yes	Green	10.1016/j.jcsr.2020.106387		
11	Article in Jo	A modified specimen holder for cone calorimeter testing	Anna Sandinge; Per Blomqvist; Mic	Fire and Materials	46/1	Yes	Green	10.1002/fam.2949		

Gestion de conflits

Dans un projet collaboratif européen

Session 3 – M3.2

Gouvernance dans un projet collaboratif EU

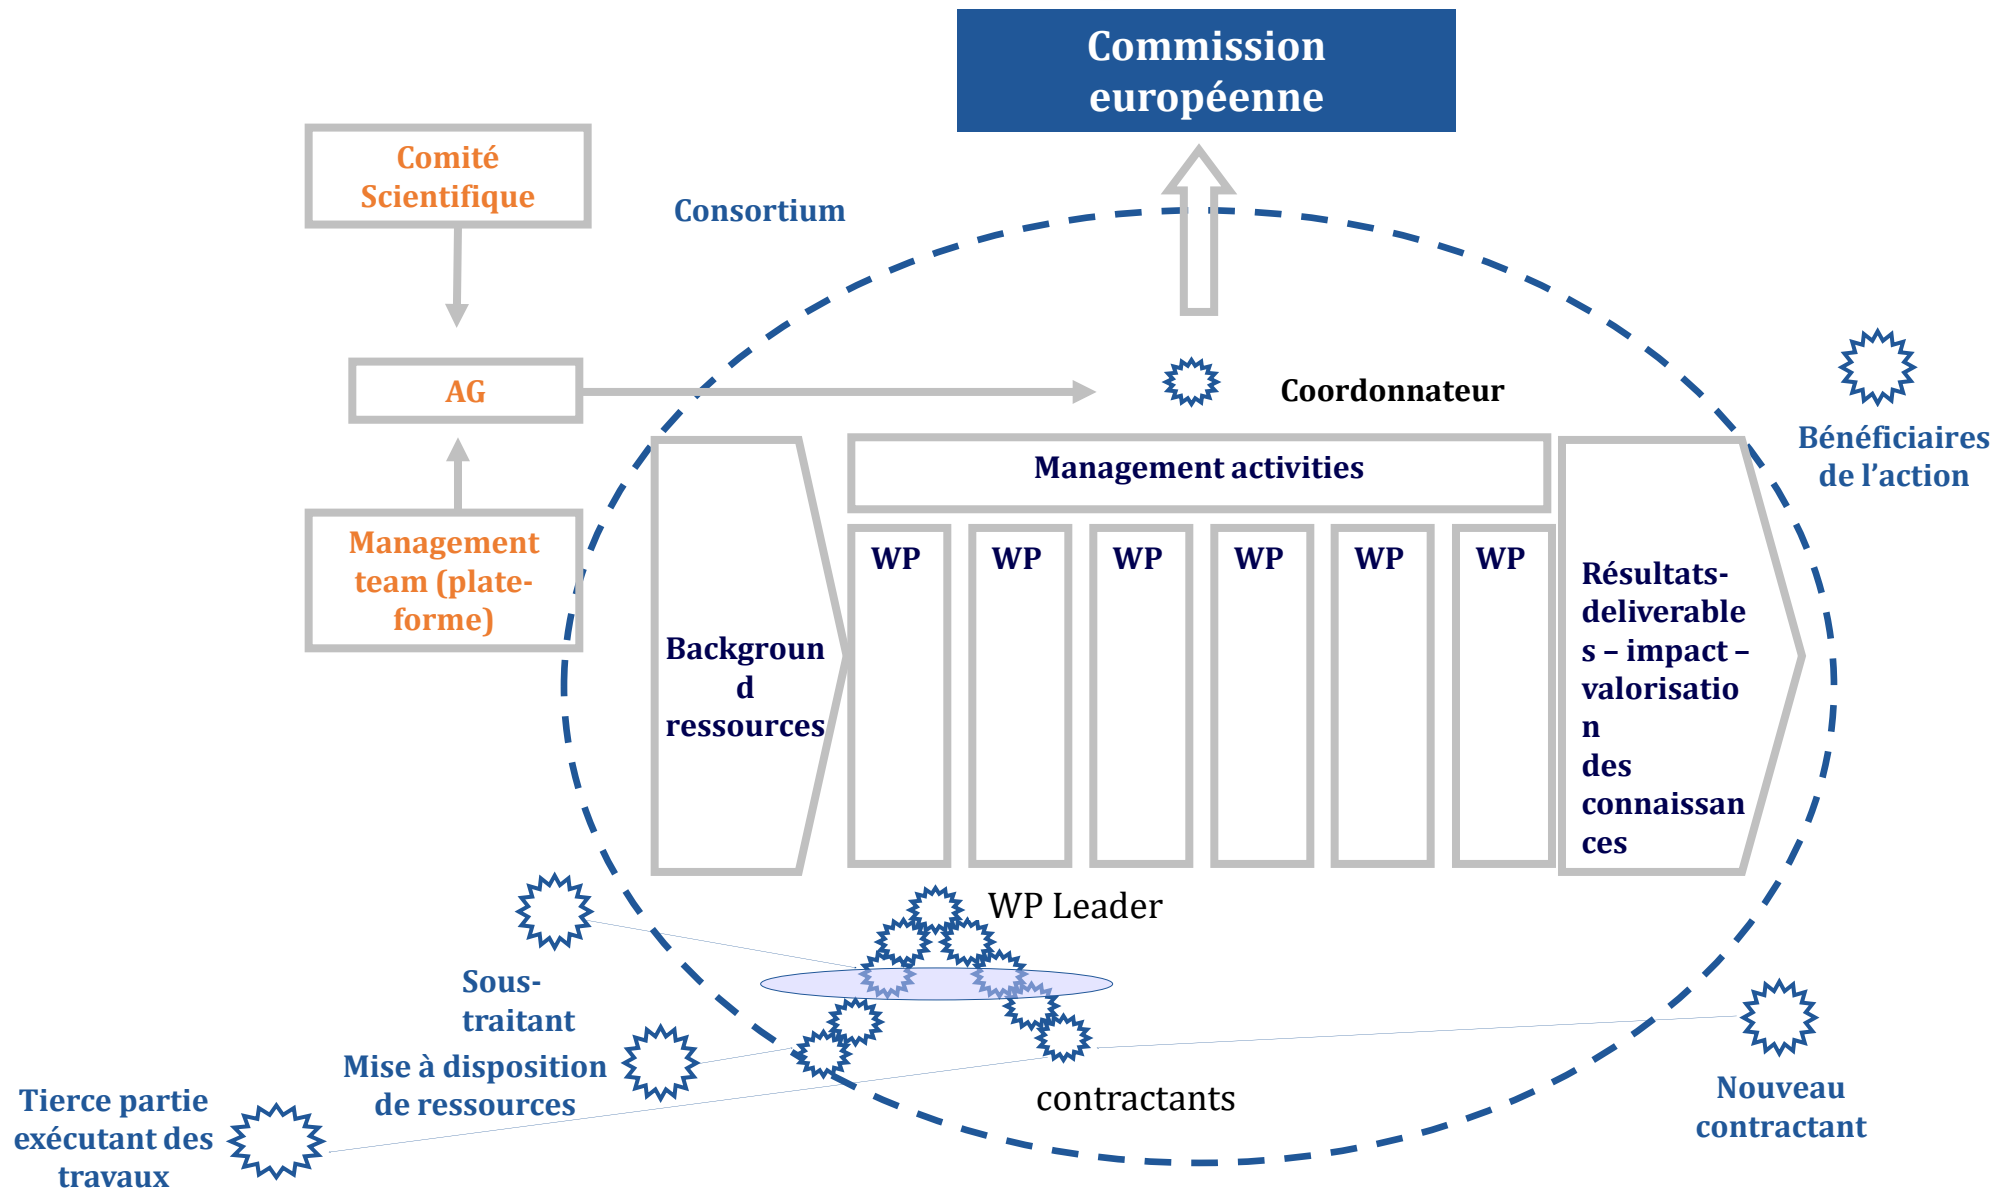

Conflits au sein du consortium

Les conflits peuvent émerger à différents niveaux :

- ✓ Évolution du consortium :
 - ✓ Divergences sur les objectifs, arrivée ou retrait de partenaires etc.
- ✓ Propriété intellectuelle :
 - ✓ Tensions entre confidentialité et diffusion, droits d'accès aux résultats etc.
- ✓ Réalisation du projet :
 - ✓ Désaccords sur la répartition du budget, des tâches, ou la gestion des livrables et paiements etc.

Résolution des conflits

- ✓ Procédures internes :
 - ✓ Recours aux comités consultatifs et vote en Assemblée générale.
- ✓ Références contractuelles :
 - ✓ Respect du Consortium Agreement et du Grant Agreement.
- ✓ Approche équitable :
 - ✓ Décisions transparentes et équilibrées.
- ✓ Conséquences à anticiper :
 - ✓ Réallocation de ressources, redéfinition des droits d'accès, voire retrait d'un partenaire.


Mise en place d'outils de gestion

Pour organiser et piloter un projet collaboratif européen

Session 3 – M3.2


Les risques dans les projets collaboratifs UE

Le risque est un danger éventuel plus ou moins prévisible qui peut affecter l'issue du projet

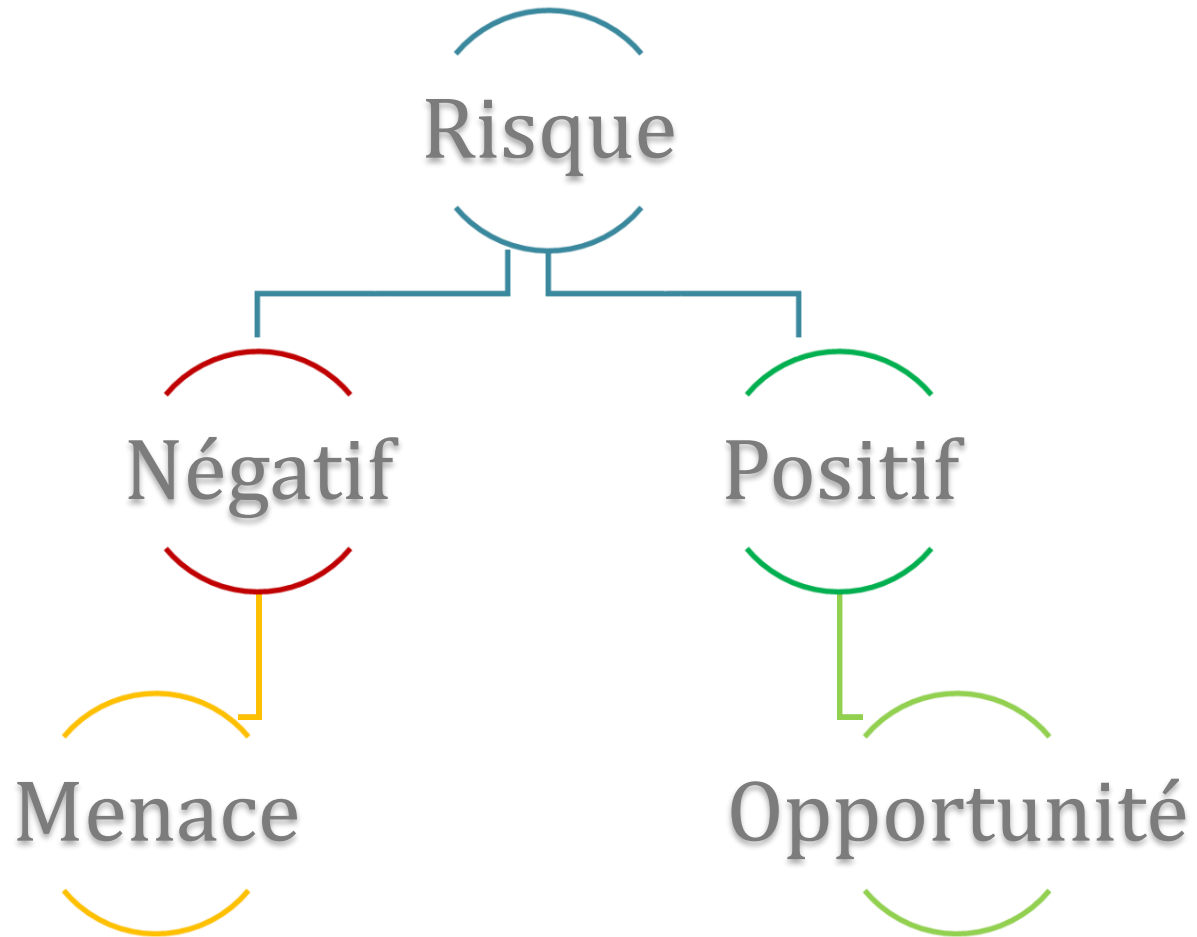

Les types de risques


Tous doivent être pris en compte sans exception dans un **registre de risque** à identifier dans votre proposition (**Section 3**)

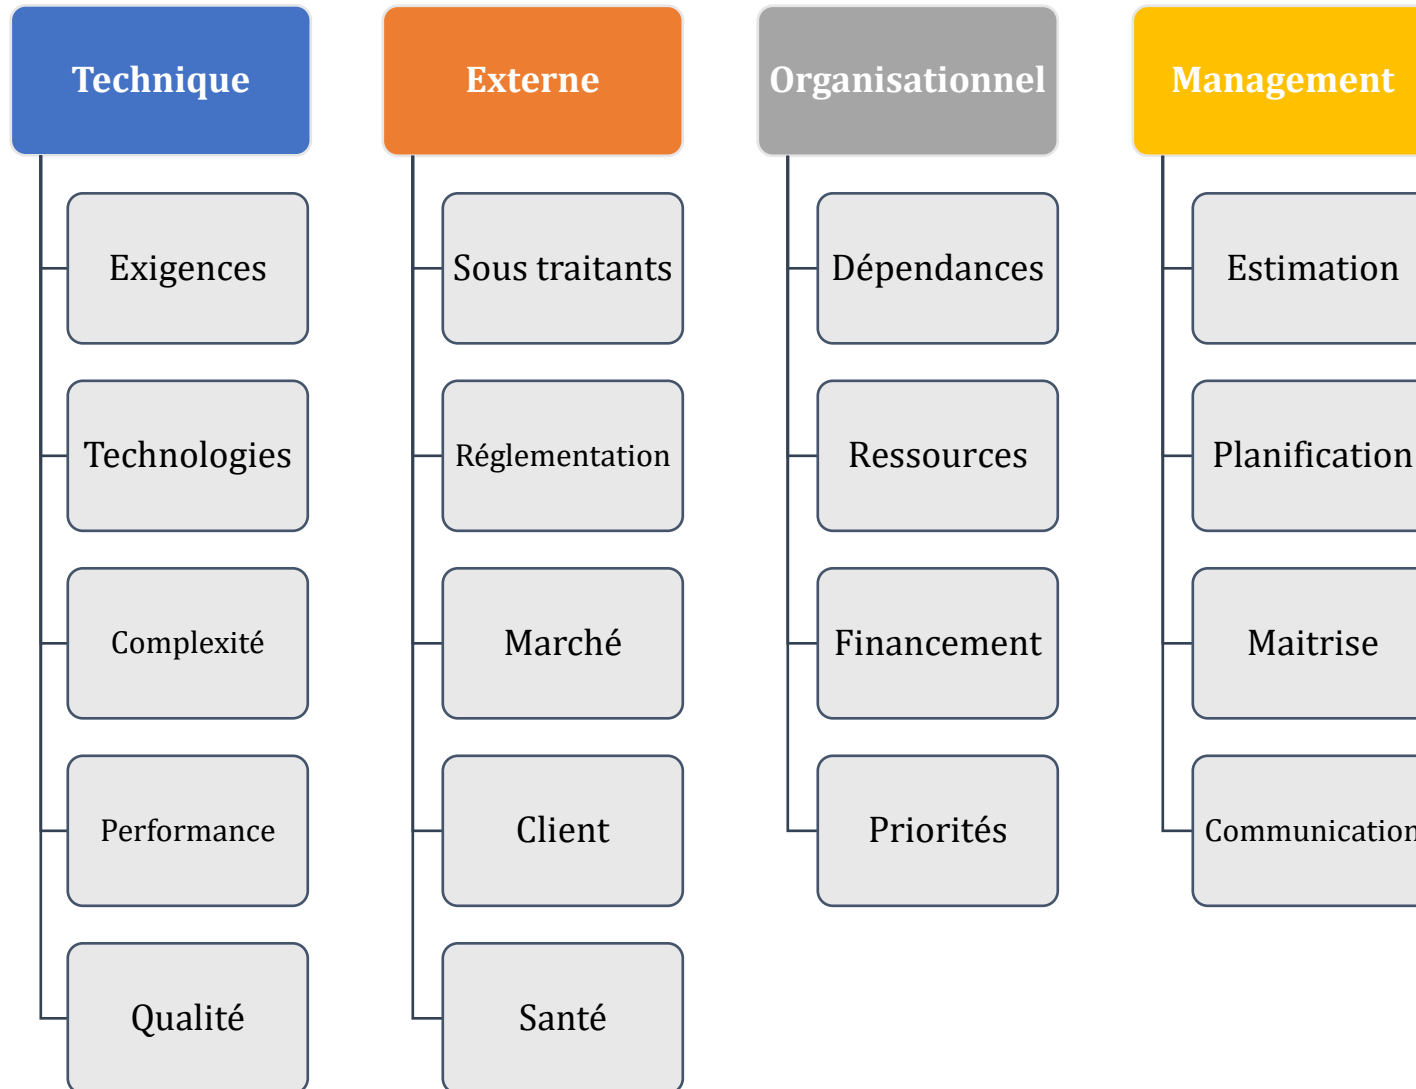

La gestion des risques

Montage : phase développement
de la proposition

Coordination : phase
d'exécution du projet

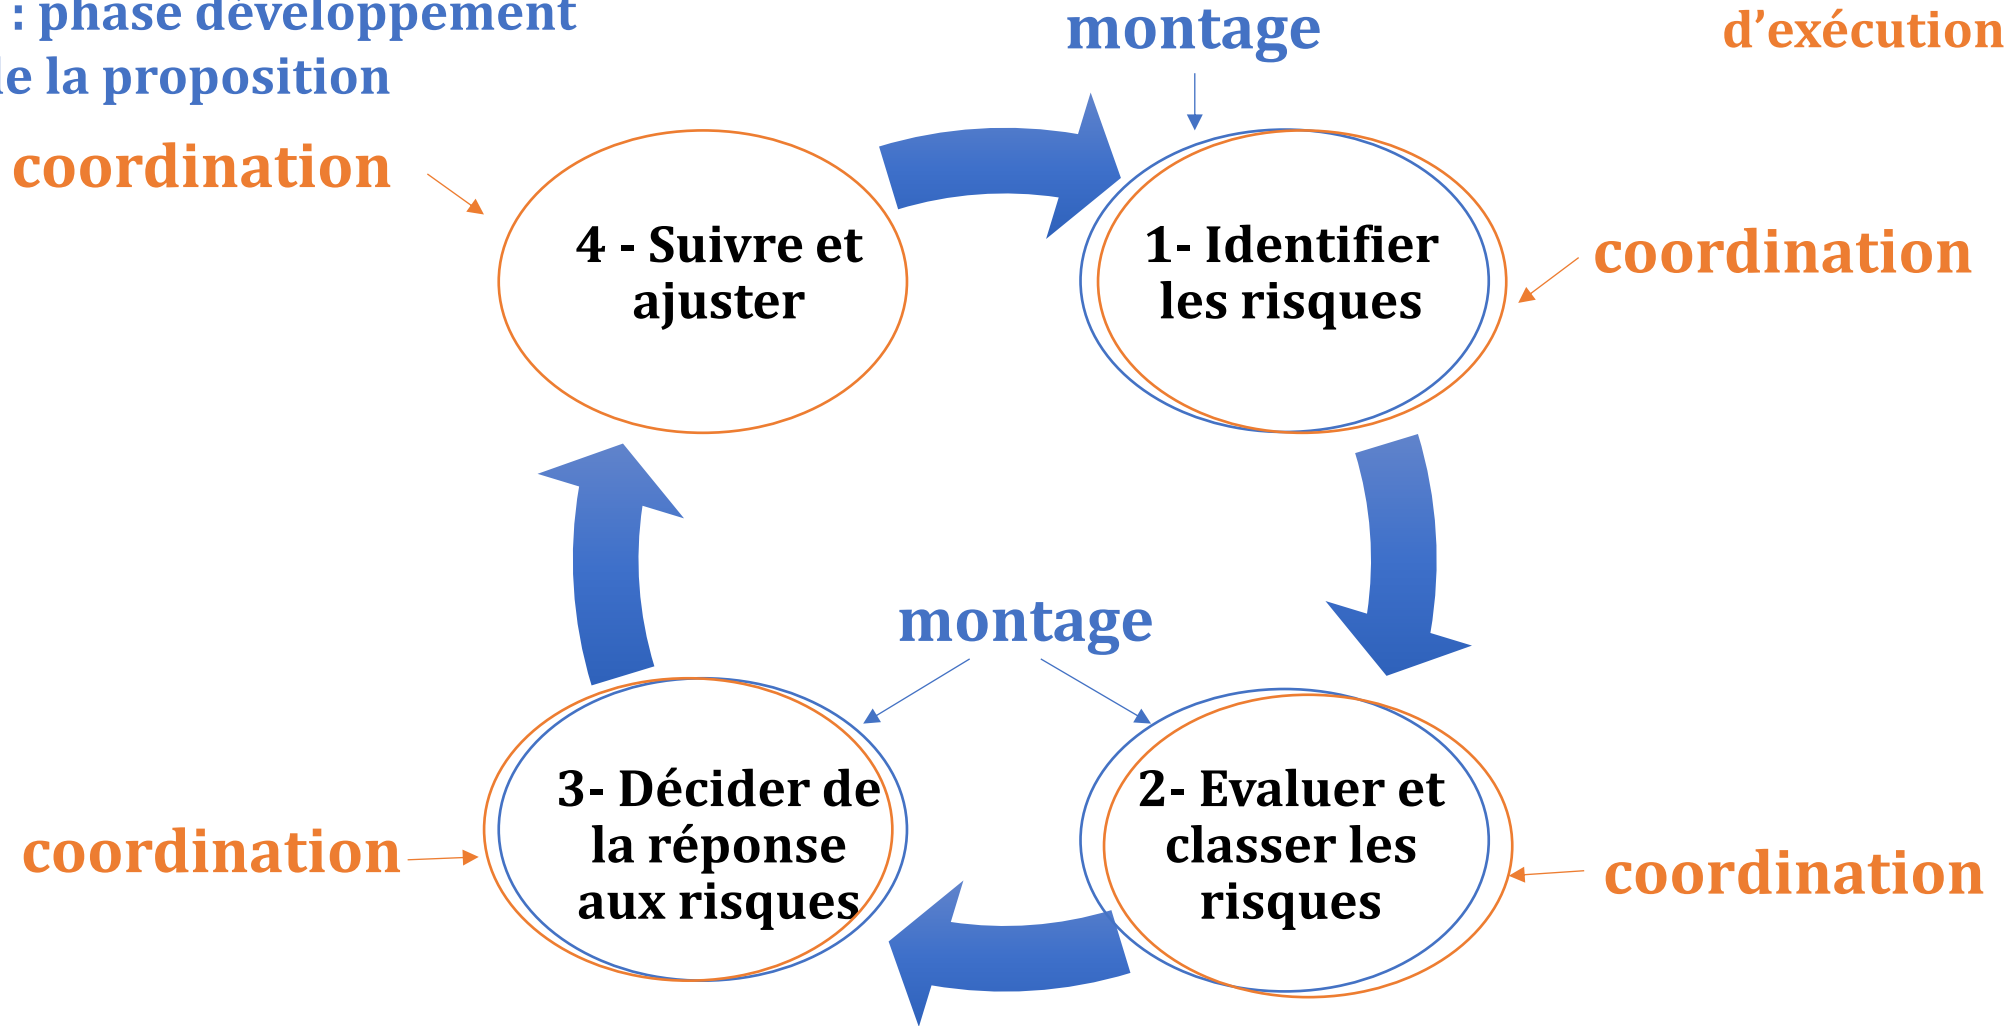

Exercices

QCM

Session 3 – M3.1



**Quel outil permet de suivre
l'avancement des tâches et des jalons
d'un projet ?**



Parmi les éléments suivants, lequel peut être une source fréquente de conflit dans un consortium ?



Quelle est la première étape de la gestion des risques dans un projet ?



Quelle stratégie est considérée comme une bonne pratique pour gérer un risque identifié ?



Programme financé
par l'Union européenne

En vous remerciant de votre participation !



Contact formateurs :
formationprojetsEB@innofluence.eu

Toutes les informations relatives à la
formation se retrouvent ici:

<https://innofluence.eu/index.php/formation-en-developpement-et-soumission-de-projets-de-recherche/>

Des questions ?

PROGRAMME
**ÉCONOMIE
BLEUE** EN ALGÉRIE
Pêche et Aquaculture



www.economiebleue.dz



www.facebook.com/ecobleue.dz



www.linkedin.com/company/programme-economie-bleue

